


Section 1: Jira Workspace Screenshots


1.1 Epics & Backlog

Three Epics were created from the Lab 1 functional requirements: (1) Spec Ingestion & Mock Generation, (2) Request Validation & Mock Responses, and (3) Testing & Observability Tools. Six User Stories were written under these Epics and assigned story points using the Fibonacci scale (3 and 5 points based on complexity).

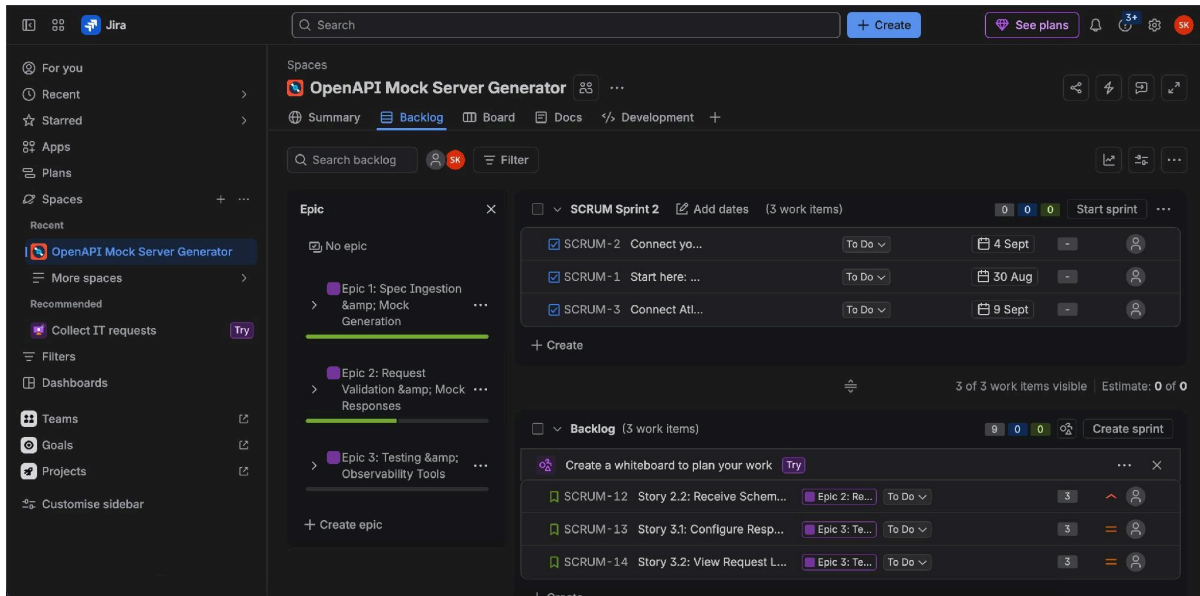

1.2 Active Sprint Board — Sprint 1

Sprint 1 (26 Aug – 2 Sep) contained Stories 1.1, 1.2, and 2.1, totalling 13 story points. The following screenshots show the board state as tasks were progressed from To Do → In Progress → Done.

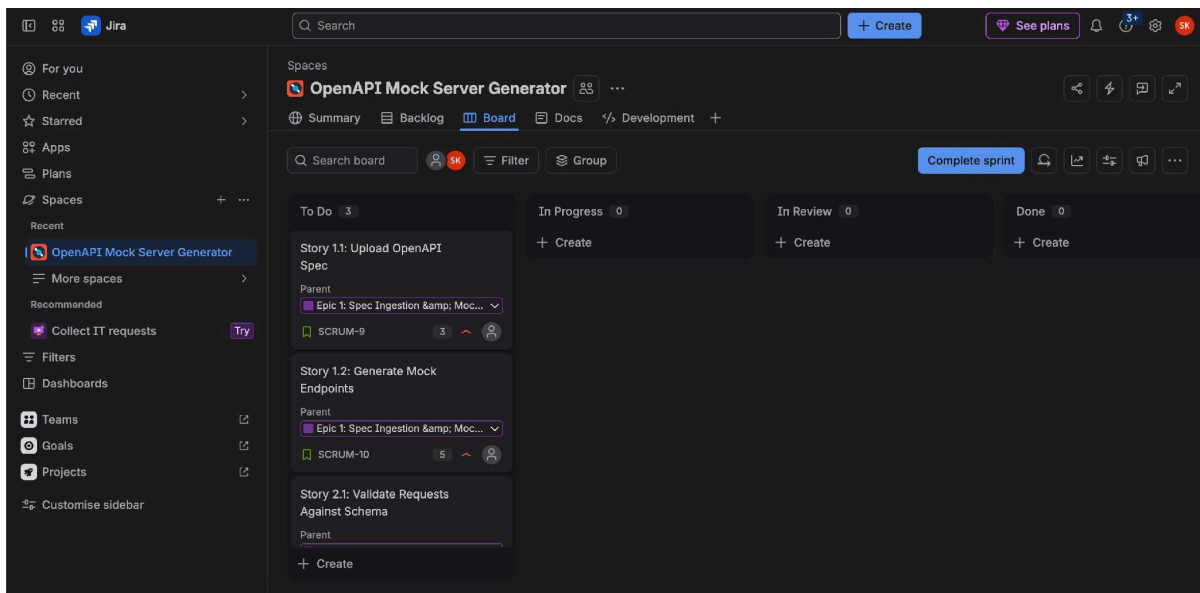

For you

Recent

Starred

Apps

Plans

Spaces

Recent

OpenAPI Mock Server Generator

More spaces

Recommended

Collect IT requests

Filters

Dashboards

Teams

Goals

Projects

Customise sidebar

Search

Create

See plans

3+

SK

Spaces

OpenAPI Mock Server Generator

Summary

Backlog

Board

Docs

Development

Search board

SK

Filter

Group

Complete sprint

...

To Do 2

Story 1.2: Generate Mock Endpoints

Parent

Epic 1: Spec Ingestion & Moc...

SCRUM-10

5

Story 2.1: Validate Requests Against Schema

Parent

Epic 2: Request Validation &...

SCRUM-11

5

+ Create

In Progress 1

Story 1.1: Upload OpenAPI Spec

Parent

Epic 1: Spec Ingestion & Moc...

SCRUM-9

3

+ Create

In Review 0

+ Create

Done 0

+ Create

For you

Recent

Starred

Apps

Plans

Spaces

Recent

OpenAPI Mock Server Generator

More spaces

Recommended

Collect IT requests

Filters

Dashboards

Teams

Goals

Projects

Customise sidebar

Search

Create

See plans

3+

SK

Spaces

OpenAPI Mock Server Generator

Summary

Backlog

Board

Docs

Development

Search board

SK

Filter

Group

Complete sprint

...

To Do 2

Story 1.2: Generate Mock Endpoints

Parent

Epic 1: Spec Ingestion & Moc...

SCRUM-10

5

Story 2.1: Validate Requests Against Schema

Parent

Epic 2: Request Validation &...

SCRUM-11

5

+ Create

In Progress 0

+ Create

In Review 0

+ Create

Done 1

Story 1.1: Upload OpenAPI Spec


Parent

Epic 1: Spec Ingestion & Moc...

SCRUM-9


3

+ Create

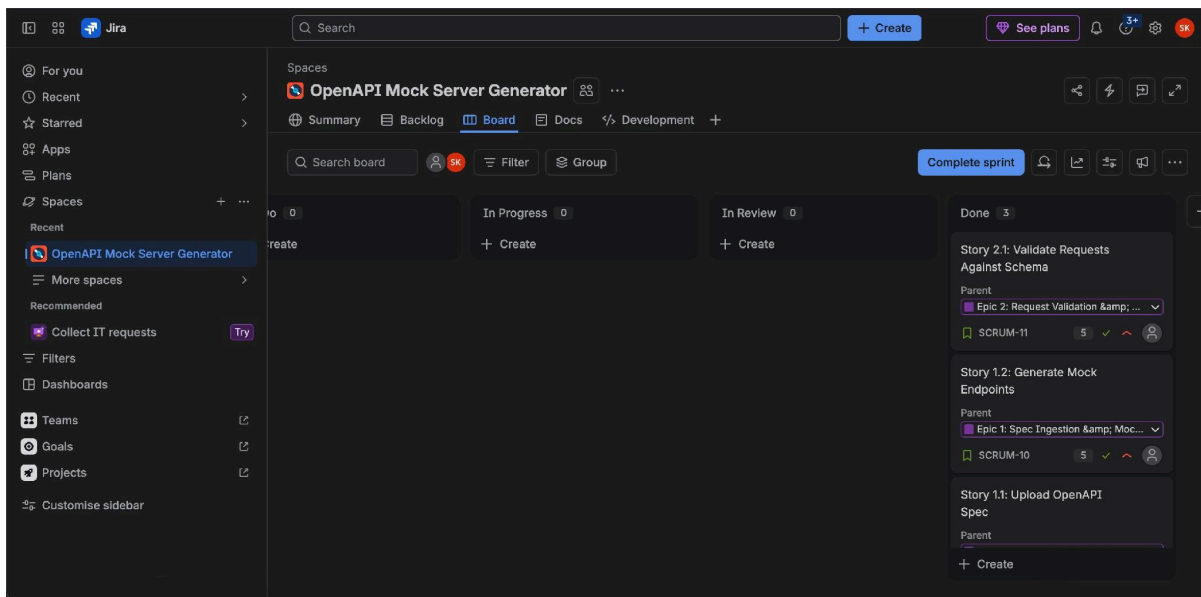



1.3 Active Sprint Board — Sprint 2


Sprint 2 carried the remaining 3 stories (2.2, 3.1, 3.2) — 9 story points in total. All were completed within the sprint window.

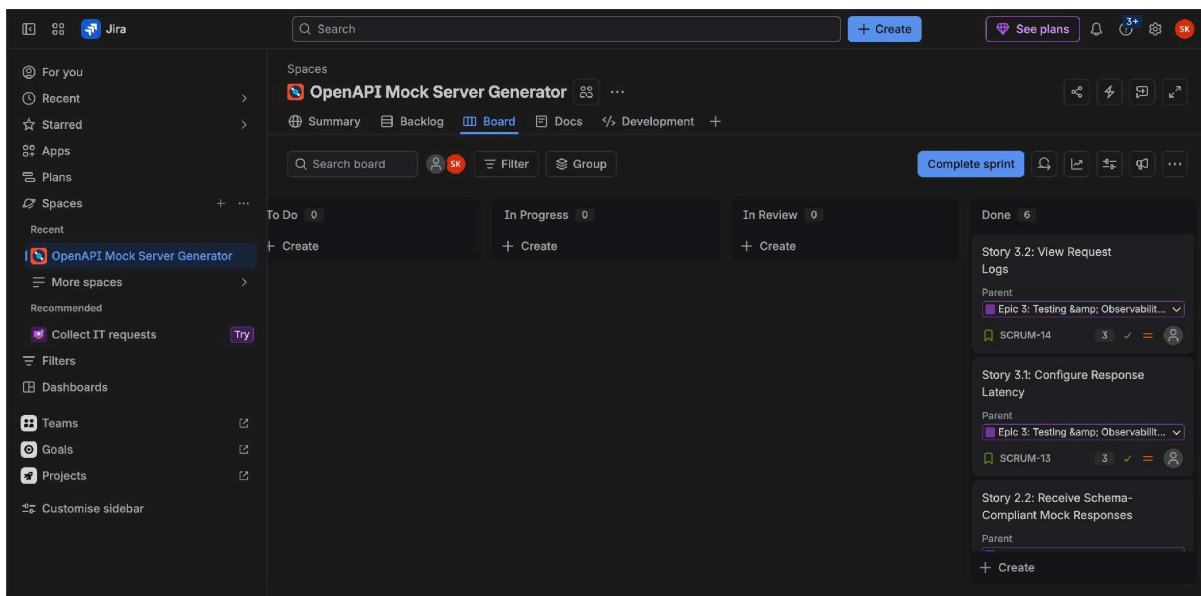

1.4 Burndown Charts

The burndown charts below show the story points remaining vs. the ideal guideline for each sprint. Because this was a simulated sprint completed in a single session, the red line drops sharply at the start — this is expected behaviour for a simulation exercise.

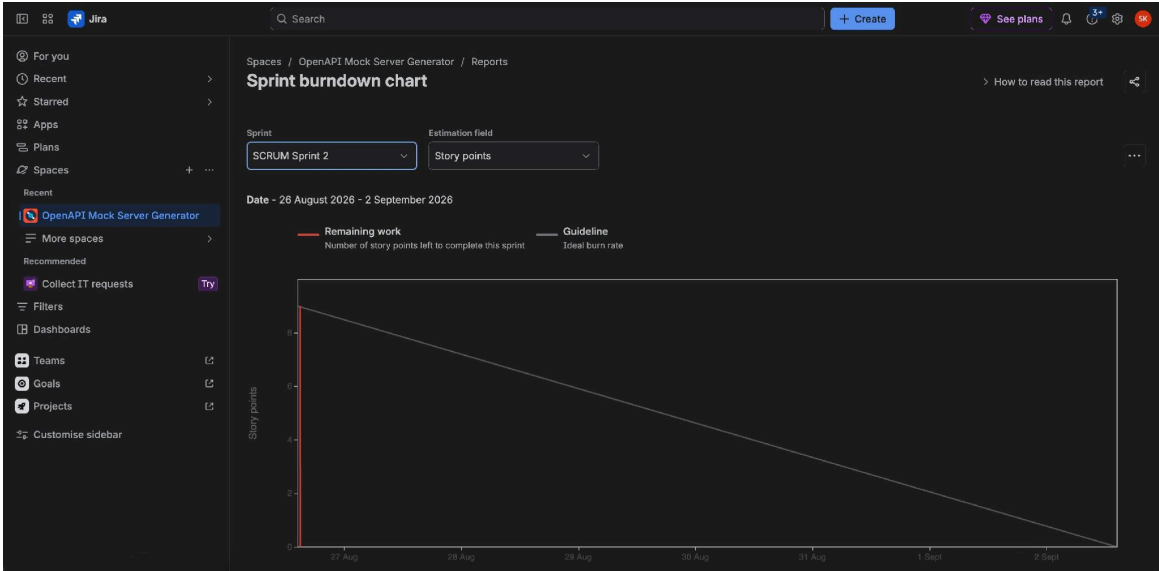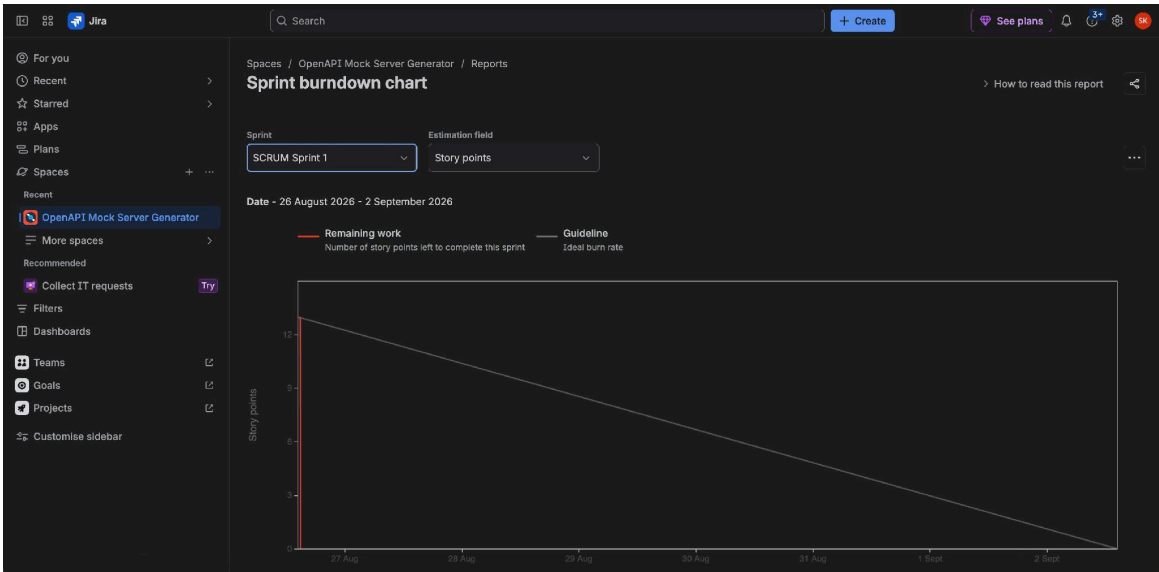

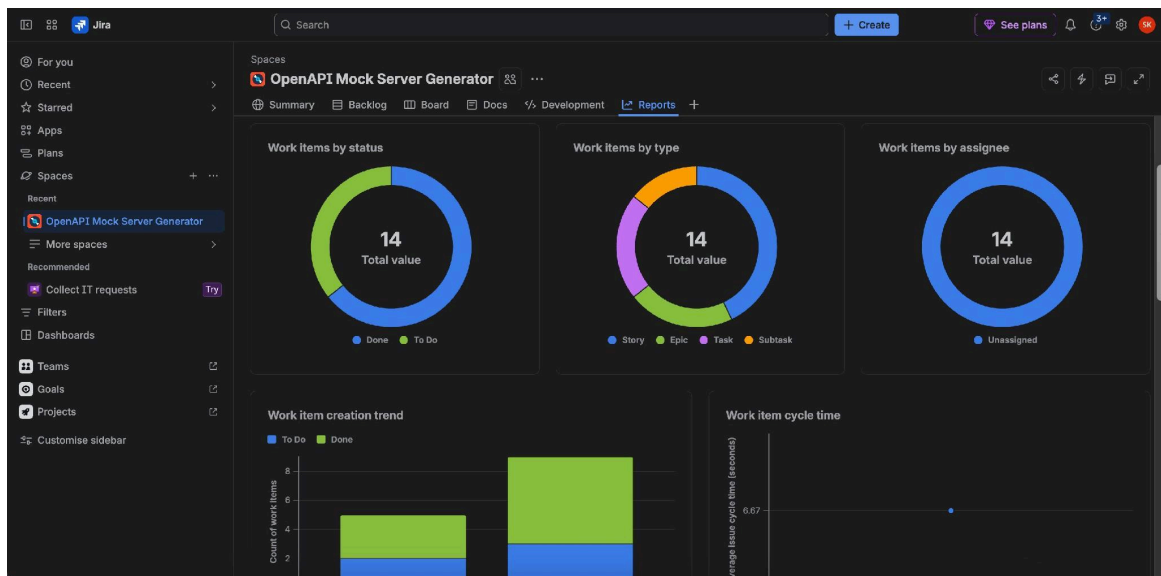

Section 2: Reflection Questions

Q1. Did your estimations reflect the actual effort?

Since this was a simulated sprint, everything got completed in one sitting, so the estimates weren't tested against real development time. That said, the relative sizing was reasonable — stories involving schema validation and endpoint generation were assigned 5 points each, which makes sense given their higher complexity. Simpler tasks like uploading a spec or viewing logs were assigned 3 points. In a real project setting, these estimates would likely hold up well as a starting baseline, though they'd be refined over time as the team built velocity data.

Q2. Was your backlog well-prioritized?

The backlog was ordered so foundational features came first — specifically, uploading a spec and generating endpoints, since every other part of the system depends on those working correctly. Schema validation and mock response logic came next, as they build directly on the generation layer. Observability features like latency configuration and request logs were placed last since they enhance the tool without blocking core functionality. High-priority items were handled in Sprint 1 and medium-priority ones in Sprint 2, which aligned well with the dependency structure.

Q3. How did your simulated sprint align with your plan?

Both sprints were completed with no spillover, which was the goal. Sprint 1 covered the core mock generation pipeline (13 points across 3 stories) and Sprint 2 covered the testing and observability features (9 points across 3 stories). The split mapped cleanly to the Epic structure. The only limitation of simulating is that all tasks were completed on day 1, which doesn't reflect a realistic development pace — but the planning structure itself was solid and logically sequenced.

Q4. What insights did the burndown chart give about team capacity?

The burndown charts showed a near-vertical drop on day 1 for both sprints, which is a direct result of the simulation — not a reflection of actual capacity. In a real sprint, the red 'remaining work' line would gradually step down over the week, ideally tracking close to the grey guideline. What the chart does confirm is that both sprints reached 0 remaining points by the end, meaning the planned scope was fully achievable within a 1-week window. Going forward, a more realistic simulation would spread task completion across multiple days so the burndown chart gives useful information about pace and whether the team is on track mid-sprint.

Jira link: <https://sameekshakumar.atlassian.net/jira/software/projects/SCRUM/boards/1/backlog?epics=visible>
